PROJECT PLANNING PHASE

Project Planning (Product Backlog, Sprint Planning, Stories, Story Points)

Date	23 October 2026	**Team ID**	
Project Name	Software Installation Request (ServiceNow Service Catalog)	**Maximum Marks**	5 Marks

Project Scope

The project automates employee requests for company-approved software through a ServiceNow Service Catalog item named **Software Installation Request**. The requester supplies the software name, version, business reason, and urgency. The request is routed for the requested employee's manager approval. If approved, a catalog task is assigned to **Software Support Team** for fulfillment. The workflow waits for the task outcome and sends a completion or license-unavailable email. A separate Business Rule, **Create Incident on License Issue**, is intended to create an incident when a Requested Item is put On Hold due to a license issue.

Product Backlog, Sprint Schedule, and Estimation

Story points are planning estimates for the scope discussed. They are not actual effort measurements or proof that every story has passed end-to-end testing.

Sprint	Functional Requirement (Epic)	User Story	User Story / Task	Story Points	Priority	Team Members
Sprint 1	Catalog Item & Request Capture	US-01	As an employee, I want to submit a Software Installation Request so that I can request approved software through the Service Catalog.	3	High	Not specified
Sprint 1	Catalog Item & Request Capture	US-02	As a requester, I want to provide software name, version, business reason, and urgency so that Software Support has the information needed to fulfill my request.	3	High	Not specified
Sprint 1	Catalog Item & Request Capture	US-03	As a project administrator, I want the catalog item organized under the Software category and Service Catalog so that employees can find it.	2	Medium	Not specified
Sprint 2	Manager Approval & Fulfillment	US-04	As an employee, I want my manager to approve or reject the request so that software installation is authorized before fulfillment.	5	High	Not specified
Sprint 2	Manager Approval & Fulfillment	US-05	As Software Support, I want an approved request to create a Catalog Task assigned to Software Support Team so that fulfillment work is tracked.	3	High	Not specified
Sprint 3	Task Outcome & Notifications	US-06	As the workflow, I want to wait until the Catalog Task is Closed Complete or Pending so that the correct outcome notification can be sent.	3	High	Not specified
Sprint 3	Task Outcome & Notifications	US-07	As a requester, I want an email confirming successful software installation so that I know the request is complete.	2	High	Not specified
Sprint 3	Task Outcome & Notifications	US-08	As a requester, I want an email when a license is unavailable, including an estimated one-week wait, so that I know why installation is delayed.	3	High	Not specified
Sprint 4	License Exception & Validation	US-09	As support staff, I want an Incident created when a Requested Item is placed On Hold for a license issue so that the issue can be tracked separately.	5	Medium	Not specified
Sprint 4	License Exception & Validation	US-10	As a tester, I want to verify request submission, manager approval, task creation, task outcomes, and notifications so that the end-to-end workflow is validated.	5	High	Not specified
Sprint 4	Release & Documentation	US-11	As the project team, I want to maintain the update set and project documentation so that the configuration and implementation can be reviewed and transferred.	3	Medium	Not specified
Sprint 4	Release & Documentation	US-12	As the project team, I want to validate the solution in the target ServiceNow instance so that the configured solution behaves consistently.	3	High	Not specified

SPRINT PLAN AND PROJECT TRACKER

Planned scope, story-point totals, schedule fields, and velocity baseline

Sprint Summary

Sprint	Planned Scope	Total Story Points
Sprint 1	Catalog item setup, request variables, and catalog organization	8
Sprint 2	Manager approval and approved-request Catalog Task creation/assignment	8
Sprint 3	Wait for task outcome and send success or license-unavailable email	8
Sprint 4	License-issue incident automation, end-to-end validation, update set, and documentation	16
TOTAL	Complete planned project backlog	40

Project Tracker

The supplied template requests sprint duration, start/end dates, completed points, and actual release dates. Those dates and actual completion figures were not provided in the project conversation, so they are marked Not scheduled or Not recorded rather than invented.

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Points Completed	Sprint Release Date (Actual)
Sprint 1	8	Not scheduled	Not scheduled	Not scheduled	Not recorded	Not recorded
Sprint 2	8	Not scheduled	Not scheduled	Not scheduled	Not recorded	Not recorded
Sprint 3	8	Not scheduled	Not scheduled	Not scheduled	Not recorded	Not recorded
Sprint 4	16	Not scheduled	Not scheduled	Not scheduled	Not recorded	Not recorded

Velocity

Velocity is the number of story points completed by the team in a sprint. The planning backlog totals **40 story points** across four proposed sprints. Actual team velocity cannot yet be calculated because no completed-sprint point totals or sprint durations were supplied. After Sprint 1, calculate average velocity as total completed story points divided by the number of completed sprints, then use the observed value to refine later sprint commitments.

Planning estimate	40 story points across 4 proposed sprints
Actual velocity	Not yet available — requires completed sprint data

BURNDOWN AND DELIVERY CONTROL

Planned remaining work and the method for tracking actual progress

Burndown Chart

The chart is an **ideal planning baseline** based on the 40-point backlog and proposed sprint allocation. It is not actual progress: no daily completion records or sprint-end actuals were supplied.

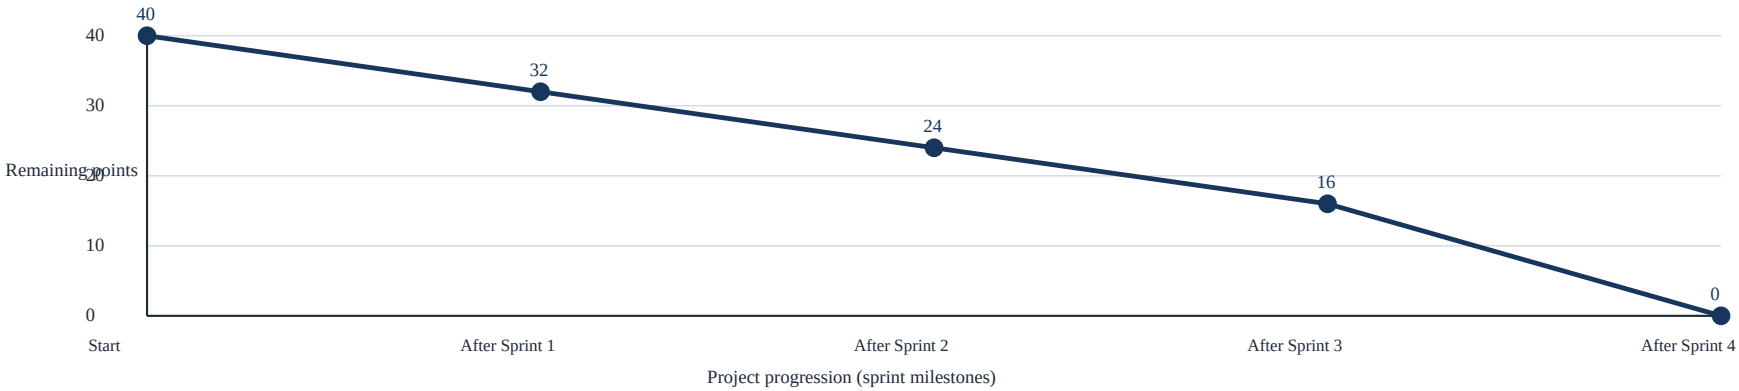

Project progression (sprint milestones)

Milestone	Planned completed	Planned remaining	Actual remaining
Project start	0	40	Not recorded
After Sprint 1	8	32	Not recorded
After Sprint 2	16	24	Not recorded
After Sprint 3	24	16	Not recorded
After Sprint 4	40	0	Not recorded

Planning Notes and Dependencies

Approval and fulfillment: Manager approval precedes Catalog Task creation. The task is assigned to **Software Support Team**; a separate Wait For Condition follows task creation, so Create Catalog Task should not itself wait.

Outcome convention: Closed Complete means successful installation; **Pending** is this project's signal for license unavailable, not a universal ServiceNow definition. The shortage email communicates an expected one-week delay.

Catalog variables: Software_Name (What software do you need?), Specify version (if required), Why do you need this software?, and Select urgency level. Get Catalog Variables exposes selected values as data pills for personalized emails.

Incident exception: The separate Business Rule, **Create Incident on License Issue**, is on Requested Item [sc_req_item], after insert/update, and is intended to create an Incident when the RITM is placed On Hold. This is separate from the Catalog Task Pending branch.

Measurement boundary: Sprint dates, duration, completed points, actual release dates, actual velocity, and actual burndown were not supplied; these remain unrecorded rather than being invented.
